

Weekly Scrum Meeting Minutes Sprint 2

===== [14:00 - 15/06/2026] Sprint 2 – Scrum Meeting #1 =====

(Author: Trần Anh Kiệt | Reviewer: Trịnh Khánh Linh | Editor: Trần Anh Kiệt)

Team members present:

- Trần Anh Kiệt
- Trần Đức Quý
- Nguyễn Quốc Dương
- Trần Minh Triết
- Trịnh Khánh Linh

Team members absent: None

Status Reports

Trần Anh Kiệt

Completed tasks:

- Draft Project Plan – Section 1, 2, 3, 4 (Deadline was 23:59, 12/06/2026).
- Vision Doc – Features: FG 1.1 User Account Management, FG 1.2 Donation Booking & Location Services (Deadline was 23:59, 14/06/2026).
- Vision Doc – Workflow Diagram: Donor Booking flow in Mermaid (Deadline was 23:59, 14/06/2026).
- Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).

To-do Tasks:

- Review & compile final Project Plan (MD + PDF) (Deadline: 23:59, 18/06/2026).
- AI Usage Report (Deadline: 23:59, 20/06/2026).
- Vision Doc - Features FG 5.1 Admin Features (Deadline: 23:59, 15/06/2026).
- Continue Self-learning: HTML + CSS + Javascript (Deadline: 23:59, 21/06/2026).

Issues/Obstacles: None reported.

Trần Đức Quý

Completed tasks:

- Vision Doc – Features: FG 1.3 Q&A AI, FG 1.4 News & Notifications (Deadline was 23:59, 14/06/2026).
- Vision Doc – Workflow Diagram: AI Feature flow in Mermaid (Deadline was 23:59, 14/06/2026).
- Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).

To-do Tasks:

- Continue Self-learning: HTML + CSS + Javascript (Deadline: 23:59, 21/06/2026).

Issues/Obstacles: None reported.

Nguyễn Quốc Dương

Completed tasks:

- Vision Doc – Section 6: Non-Functional Requirements (quantifiable: performance, security, platform) (Deadline was 23:59, 12/06/2026).
- Vision Doc – Features: FG 3.1 SOS Hospital Emergency Request Management (Deadline was 23:59, 14/06/2026).
- Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).

To-do Tasks:

- Continue Self-learning: HTML + CSS + Javascript (Deadline: 23:59, 21/06/2026).

Issues/Obstacles: None reported.

Trần Minh Triết

Completed tasks:

- Vision Doc – Features: FG 2.1 Campaign & Donor Management, FG 2.2 Communication & Engagement Management, FG 2.3 Blood Inventory & Emergency Coordination, FG 4.1 User Automations, FG 4.2 BC Automations (Deadline was 23:59, 14/06/2026).
- Vision Doc – Workflow Diagram: SOS Emergency flow in Mermaid (Deadline was 23:59, 14/06/2026).
- Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).

To-do Tasks:

- Spec Kit GitHub Team Repo setup + constitution.md (Deadline: 23:59, 15/06/2026).

- Continue Self-learning: HTML + CSS + Javascript (Deadline: 23:59, 14/06/2026).

Issues/Obstacles: None reported.

Trịnh Khánh Linh

Completed tasks:

- Vision Doc – Section 1, 2, 3, 4 (Deadline was 23:59, 12/06/2026).
- Vision Doc – Features: FG 1.5 Donation Impact & Tracking, FG 1.6 Community (Deadline was 23:59, 14/06/2026).
- Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).

To-do Tasks:

- Review & compile final Vision Document (MD + PDF) (Deadline: 18/06/2026).
- Continue Self-learning: HTML + CSS + Javascript (Deadline: 23:59, 21/06/2026).

Issues/Obstacles: None reported.


Actions (if any):

Action Item	Owner	Deadline
Review & compile final Project Plan (MD + PDF)	Kiệt	23:59, 18/06/2026
Review & compile final Vision Document (MD + PDF)	Linh	23:59, 18/06/2026
Spec Kit GitHub setup + constitution.md + training evidence	All members individually	23:59, 14/06/2026
Continue Self-learning: HTML + CSS + Javascript	All members individually	23:59, 21/06/2026
AI Usage Report	Kiệt	23:59, 20/06/2026
Sprint Review Meeting & PA2 submission	All members	21/06/2026
Vision Doc - Features FG 5.1 Admin Features	Kiệt	23:59, 15/06/2026
Spec Kit GitHub Team Repo setup + constitution.md	Triết	23:59, 15/06/2026


Summary of the meeting:

The team convened for the first Scrum meeting of Sprint 2 to review task progress against the Sprint Planning schedule. Members reported that all hard-deadline drafts due by 12/06/2026 (Project Plan Sections 1–4 and Vision Doc Sections 1–4 and Section 6) have been completed as planned. Vision Doc Section 5 feature write-ups (all 12 functional groups) and the three Mermaid workflow diagrams are either completed or in final review, with most members on track for the 14/06/2026 deadline. The team was reminded that the compilation and review phase for both the Project Plan and the Vision Document must be finalized by 18/06/2026 to allow sufficient buffer before the Sprint Review Meeting and PA2 submission on 21/06/2026. Spec Kit initialization and self-learning tasks were noted as ongoing for all members. No blockers were reported.

Picture of meeting:

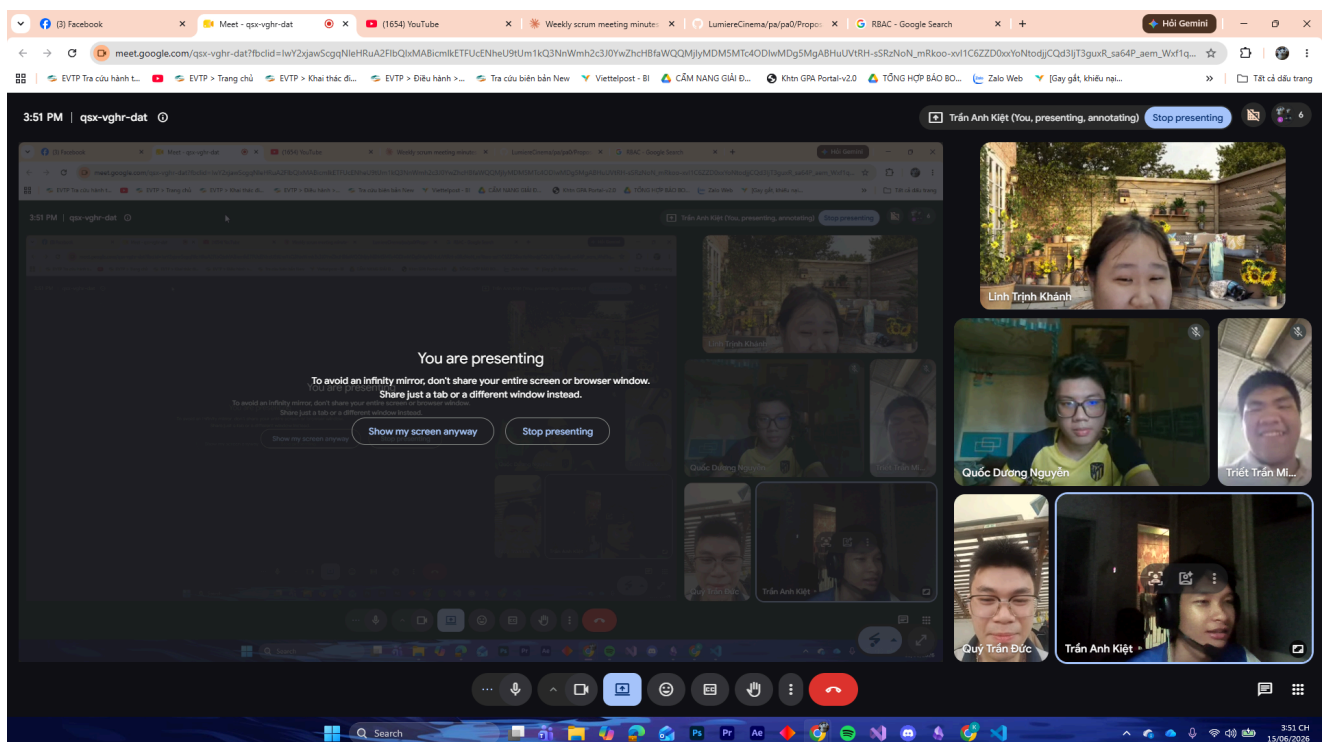

Screenshot of all tasks:

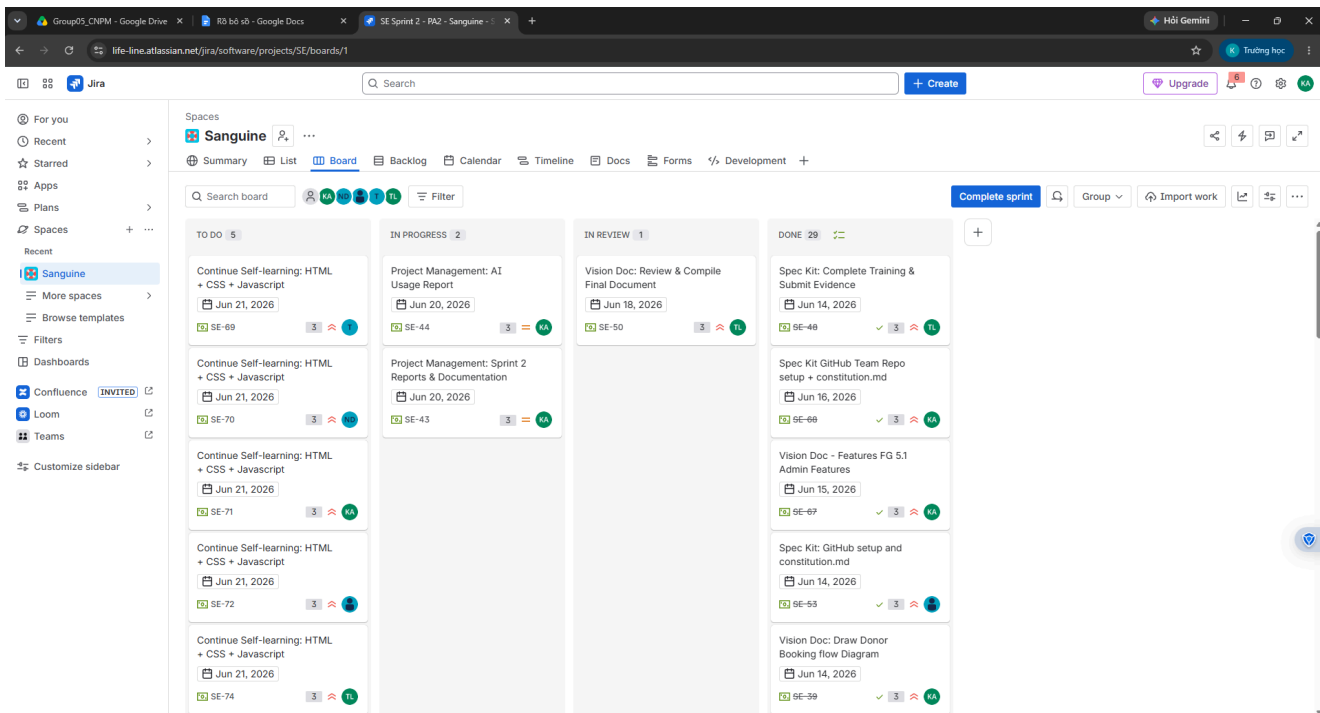

===== [20:00 18/06/2026] Sprint 2 - Scrum Meeting #2 =====

(Author: Trần Anh Kiệt | Reviewer: Trịnh Khánh Linh | Editor: Trần Anh Kiệt)

Team members present:

- Trần Anh Kiệt
- Trần Đức Quý
- Nguyễn Quốc Dương
- Trần Minh Triết
- Trịnh Khánh Linh

Team members absent:

- None

Status Reports:

Trần Anh Kiệt

- Completed tasks:
 - Vision Doc - Features FG 5.1 Admin Features (Deadline was 23:59, 15/06/2026).
 - Draft Project Plan – Section 1, 2, 3, 4 (Deadline was 23:59, 12/06/2026).
 - Vision Doc – Features: FG 1.1 User Account Management, FG 1.2 Donation Booking & Location Services (Deadline was 23:59, 14/06/2026).
 - Vision Doc – Workflow Diagram: Donor Booking flow in Mermaid (Deadline was 23:59, 14/06/2026).
 - Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).
- To-do Tasks:
 - Review & compile final Project Plan (MD + PDF) (Deadline 23:59, 18/06/2026).
 - UC Diagrams - User Features 1.1-1.6 (Mermaid) (Deadline: 23:59, 21/06/2026).

- UC Spec - 1.1 User Account Mgmt & 1.2 Donation Booking & Location (Deadline: 23:59, 21/06/2026).
- BE setup: Node.js + Python API scaffold (Deadline: 23:59, 25/06/2026).
- Implement FG1-1.1 User Account Mgmt (Backend + Spec Kit) (Deadline: 23:59, 28/06/2026).
- AI Usage Report (Deadline: 23:59, 30/06/2026).
- Issues/Obstacles: None reported.

Trần Đức Quý

- Completed tasks:
 - Continue Self-learning: HTML + CSS + Javascript.
 - Vision Doc – Features: FG 1.3 Q&A AI, FG 1.4 News & Notifications (Deadline was 23:59, 14/06/2026).
 - Vision Doc – Workflow Diagram: AI Feature flow in Mermaid (Deadline was 23:59, 14/06/2026).
 - Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).
- To-do Tasks:
 - UC Spec - 1.3 Q&A AI & 1.4 News, Notifications & SOS Emergency Alerts (Deadline: 23:59, 21/06/2026).
 - UC Diagrams - Admin Features 5.1 (Mermaid) (Deadline: 23:59, 21/06/2026).
 - UI Prototypes for all 13 FGs (Figma/v0/Bolt) (Deadline: 23:59, 25/06/2026).
- Issues/Obstacles: None reported.

Nguyễn Quốc Dương

- Completed tasks:
 - Continue Self-learning: HTML + CSS + Javascript.
 - Vision Doc – Section 6: Non-Functional Requirements (quantifiable: performance, security, platform) (Deadline was 23:59, 12/06/2026).
 - Vision Doc – Features: FG 3.1 SOS Hospital Emergency Request Management (Deadline was 23:59, 14/06/2026).
 - Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).
- To-do Tasks:
 - UC Diagrams - Hospital 3.1 (Deadline: 23:59, 21/06/2026).
 - UC Spec - 3.1 Emergency SOS Request Mgmt (Hospital) (Deadline: 23:59, 21/06/2026).
 - DB setup: MongoDB schemas (User, Donation, Campaign, Blood Bag) (Deadline: 23:59, 25/06/2026).
 - Implement FG1-1.1 User Account Mgmt (Database + Spec Kit) (Deadline: 23:59, 28/06/2026).
- Issues/Obstacles: None reported.

Trần Minh Triết

- Completed tasks:
 - Spec Kit GitHub Team Repo setup + constitution.md (Deadline was 23:59, 15/06/2026).
 - Vision Doc – Features: FG 2.1 Campaign & Donor Management, FG 2.2 Communication & Engagement Management, FG 2.3 Blood Inventory & Emergency Coordination, FG 4.1 User Automations, FG 4.2 BC Automations (Deadline was 23:59, 14/06/2026).
 - Vision Doc – Workflow Diagram: SOS Emergency flow in Mermaid (Deadline was 23:59, 14/06/2026).
 - Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).
- To-do Tasks:
 - UC Diagrams - Blood Center 2.1-2.3 (Deadline: 23:59, 21/06/2026).
 - UC Spec - 2.1 Campaign & Donor Mgmt, 2.2 Communication & Engagement, 2.3 Blood Inventory, 4.1 User Automations + 4.2 BC Automations (Deadline: 23:59, 21/06/2026).
 - UI Prototypes for all 13 FGs (Figma/v0/Bolt) (Deadline: 23:59, 25/06/2026).
 - Implement FG1-1.1 User Account Mgmt (Frontend + Spec Kit) (Deadline: 23:59, 28/06/2026).
- Issues/Obstacles: None reported.

Trịnh Khánh Linh

- Completed tasks:
 - Vision Doc – Section 1, 2, 3, 4 (Deadline was 23:59, 12/06/2026).
 - Vision Doc – Features: FG 1.5 Donation Impact & Tracking, FG 1.6 Community (Deadline was 23:59, 14/06/2026).
 - Spec Kit training evidence submission (Deadline was 23:59, 14/06/2026).
- To-do Tasks:
 - UC Spec - 1.5 Donation Impact & Tracking and 1.6 Community (Deadline: 23:59, 21/06/2026).
 - Review & compile final Vision Document (MD + PDF) (Deadline 23:59, 18/06/2026).
 - FE setup: React + Tailwind CSS project scaffold (Deadline: 23:59, 25/06/2026).
- Issues/Obstacles: None reported.

Actions (if any):

Actions (if any):

Action Item	Owner	Deadline
Disseminate and comply with the Spec Kit workflow on the shared GitHub repo	All members	Ongoing
Review & compile final Project Plan and Vision Document	Kiệt, Linh	23:59, 18/06/2026
Complete UC Diagrams (Mermaid) for all 13 FGs	All members	23:59, 21/06/2026
Complete UC Specs & UI Prototypes for all 13 FGs	All members	23:59, 21/06/2026 (UC Specs) 23:59, 25/06/2026 (UI Prototypes)
Setup Project Scaffold (FE, BE, DB)	Kiệt, Dương, Linh	23:59, 25/06/2026
Implement FG1-1.1 User Account Mgmt (Full-stack + Spec Kit)	Kiệt, Triết, Dương	23:59, 28/06/2026
AI Usage Report & Video demo FG1 (YouTube Unlisted)	Kiệt, All members	23:59, 30/06/2026

Summary of the meeting:

Today, the team completed the review and finalization of the key documents for PA2 (Project Plan and Vision Document). The meeting primarily focused on walking through the Spec Kit workflow directly on the team's shared GitHub repository, ensuring that all members fully understand how to use spec-kit and follow the proper code commit flow. Additionally, the Project Manager assigned all major tasks for Sprint 3 (PA3) in strict alignment with the Project Plan. These tasks include creating Use Case Diagrams using Mermaid, drafting Use Case Specifications alongside UI Prototypes, and initiating the project scaffold setup (FE, BE, DB) to begin implementing Functional Group 1.1 (User Account Management).

Picture of meeting:



Screenshot of all tasks:

